


PHASE 1 - INDEPENDENCE PARK MAIN LIBRARY

NOTES & MILESTONES

1070	Notice to Proceed	0	11/01/11		◆ Notice to Proceed
1060	Phase 1 Completion	0		07/04/13	◆ Phase 1 Completion

FOUNDATION/DECK POURS

1430	Building Pad Fill	0	11/21/11	01/06/12
3170	Layout Pile, Caps and Grade beams	20	12/05/11	02/27/12
1580	Load Test Pile	0	12/20/11	12/20/11
1590	Drive Piles	25	01/09/12	02/24/12
1620	Excavate Pile Caps	20	01/27/12	02/24/12
1710	Pile Cap Reinforcing	20	01/31/12	02/28/12
1820	Pour Pile Caps	35	01/31/12	03/20/12
1630	Excavate Grade Beams	25	02/07/12	03/13/12
1830	Grade Beam Reinforcing	25	02/14/12	03/20/12
3309	Form Column Pedestals/Set Anchor	20	02/20/12	03/19/12
1840	Pour Grade Beams/Column Pedestals	40	02/28/12	04/24/12
1870	Form Slab	70	04/11/12	07/18/12
1890	Slab Reinforcing	70	05/02/12	08/08/12
1680	Plumbing/Electrical Slab Rough Ins	70	05/03/12	08/09/12
1900	Slab on Grade Pour 01	5	05/04/12	05/11/12
1905	Slab on Grade Pour 02	5	05/11/12	05/18/12
3750	2nd Floor-Pour 01	5	05/18/12	05/25/12
3760	2nd Floor-Pour 02	5	05/25/12	06/01/12
3790	3rd Floor-Pour 01	5	06/01/12	06/08/12
3800	3rd Floor-Pour 02	5	06/08/12	06/15/12
3820	Roof Deck-Pour 01	5	06/15/12	06/22/12
3830	Roof Deck-Pour 02	5	06/22/12	06/29/12
1915	Slab on Grade Pour 03	5	06/29/12	07/06/12
1925	Slab on Grade Pour 04	5	07/06/12	07/13/12
3770	2nd Floor-Pour 03	5	07/13/12	07/20/12
3780	2nd Floor-Pour 04	5	07/20/12	07/27/12
3810	3rd Floor-Pour 03	5	07/27/12	08/03/12
3840	Roof Deck - Pour 03	5	08/03/12	08/10/12
3850	Roof Deck - Pour 04	5	08/10/12	08/17/12

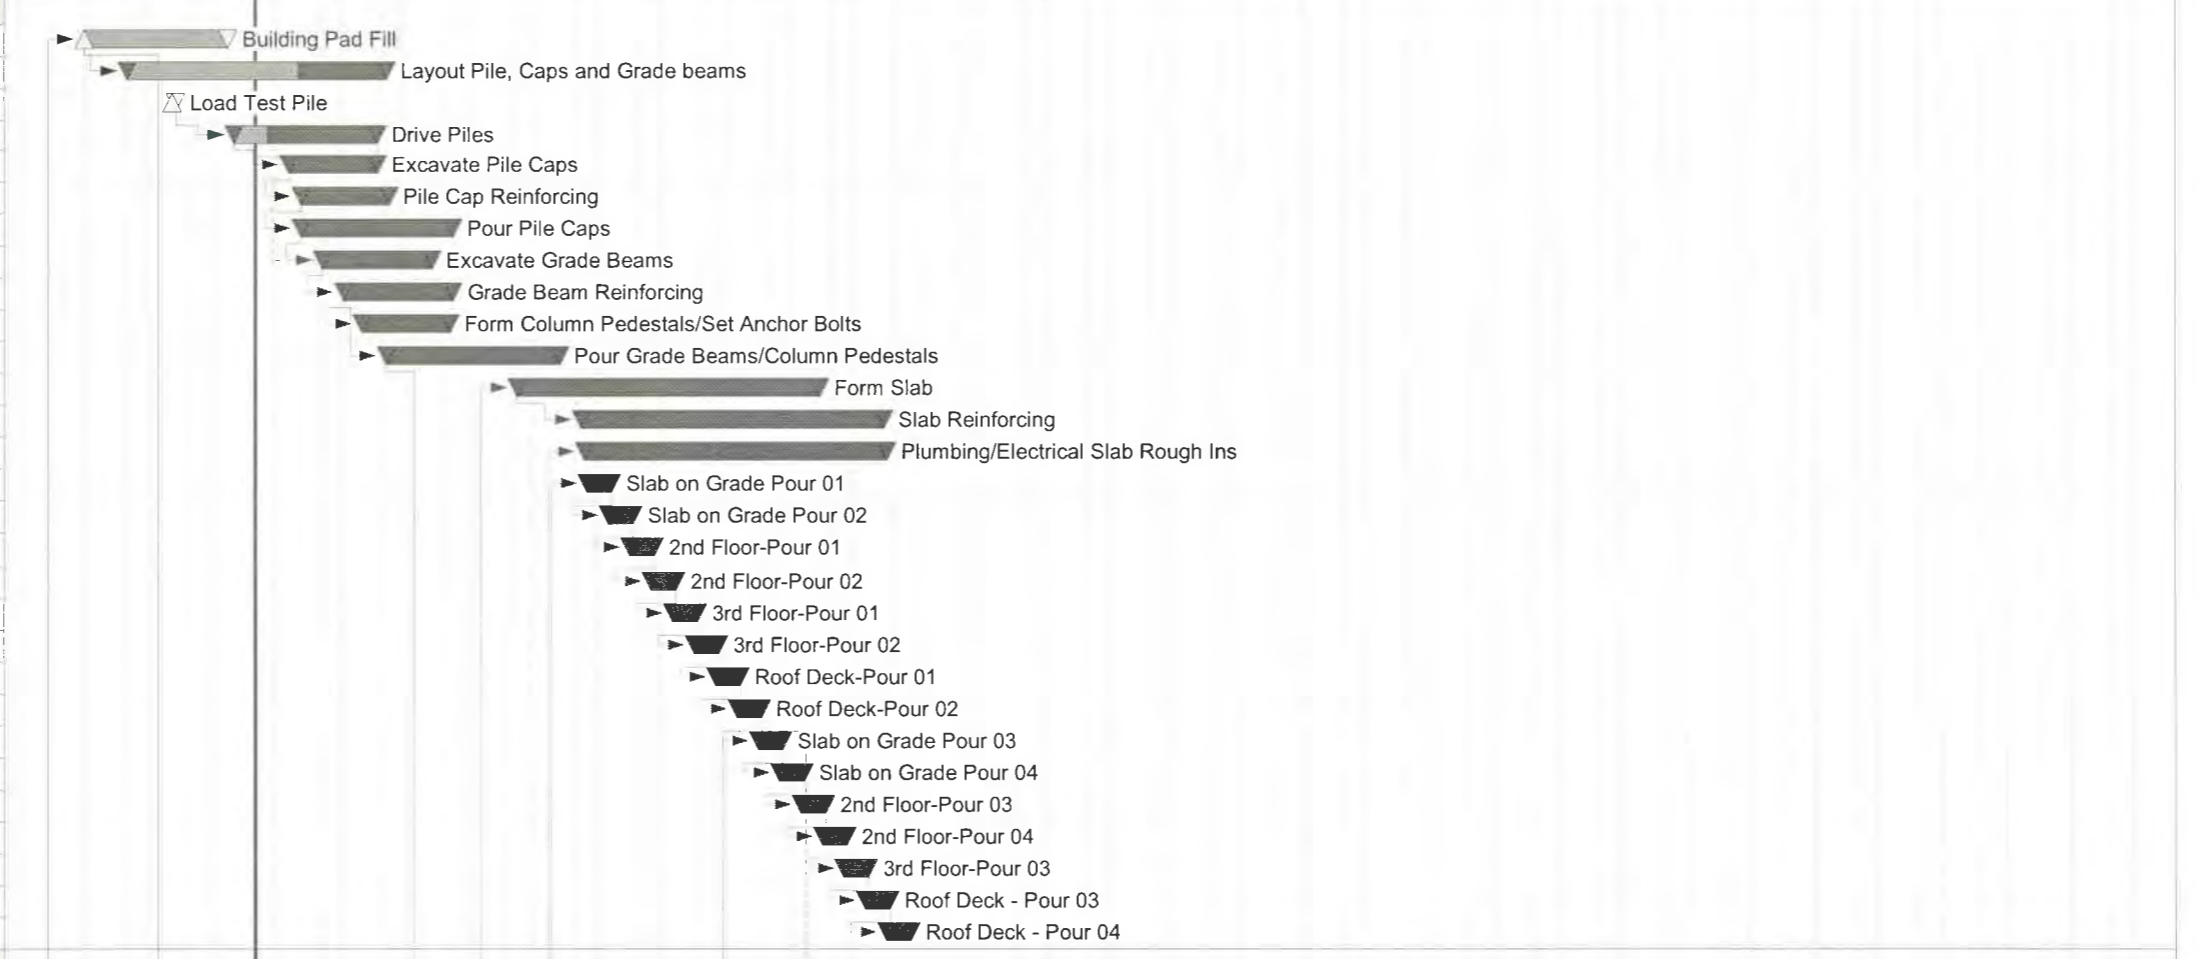

STRUCTURE

3318	COLUMN LINE A01 TO A05	1	03/20/12	03/21/12
3320	Sequence 1 - 2nd Floor Framing	5	03/21/12	03/28/12
3330	Sequence 2 - 3rd Floor Framing	5	03/28/12	04/04/12
3340	Sequence 3 - Roof Framing	5	04/04/12	04/11/12
3345	COLUMN LINES A05 TO A08	1	04/11/12	04/12/12
3350	Sequence 4 - 2nd Floor Framing	5	04/12/12	04/19/12
3360	Sequence 5 - 3rd Floor Framing	5	04/19/12	04/26/12
3370	Sequence 6 - Roof Framing	5	04/26/12	05/03/12
3380	Sequence 7 - Butterfly Roof Framing	5	05/03/12	05/10/12
3385	COLUMN LINES A08 TO A11	1	05/10/12	05/11/12
3390	Sequence 8 - 2nd Floor Framing	5	05/11/12	05/18/12
3400	Sequence 9 - 3rd Floor Framing	5	05/18/12	05/25/12
3410	Sequence 10 - Roof Framing	5	05/25/12	06/01/12
3420	Sequence 11 - Butterfly Roof Framing	5	06/01/12	06/08/12



Start date 11/01/11 4:00PM

Finish date 12/31/13 3:59PM

Data date 01/16/12 4:00PM

Run date 01/19/12 3:00PM

Page number 1A

Independence Park Main Library
Milton J. Womack, Inc.



