
WHLC Architecture - Schwartz/Silver Architects

A Joint Venture

CONSTRUCTION REPORT

Project: River Center Branch Library

Project No.: 11-025

Report No.: 029

Site Visit Date/Time: 02-08-2018

Location: Project Site; site visit and walk

Attendees: R. Roussel, T. Colomb, T. Mathis, M. Caillouet

Weather/Temp: Partly Cloudy and Warm. Mid 70s.

Work in Progress/Observations:

- Further coordination was taking place regarding the overhead grilles and overhead doors, also the framing above the accordion-style folding fire doors.
- The TPO roofing needs the proper termination. The small metal term flashing needs to be removed and ensure that all holes, punctured areas are filled and re-sealed with liquid applied air barrier.
- We met on site to discuss the detail regarding roofing and curtain wall guardrail and curb with pavers.
- The roofing needs to be cleaned off completely with no dirt or debris on the roof.
- All holes in the exterior sheathing and liquid applied need to be patched, taped with mesh tape and resealed with liquid applied before any rain screen is applied to the wall.
- Curtain wall and storefront continues to be installed.
- The HVAC work has not been connected to the units yet, and we still do not have temporary air on in the building.
- Taping and floating continues on the project.

(see attached photos)

Items/Questions:

Prepared by: WHLC Architecture, LLC.



IMG_9855



IMG_9857



IMG_9860



IMG_9862




IMG_9866



IMG_9868



IMG_9869

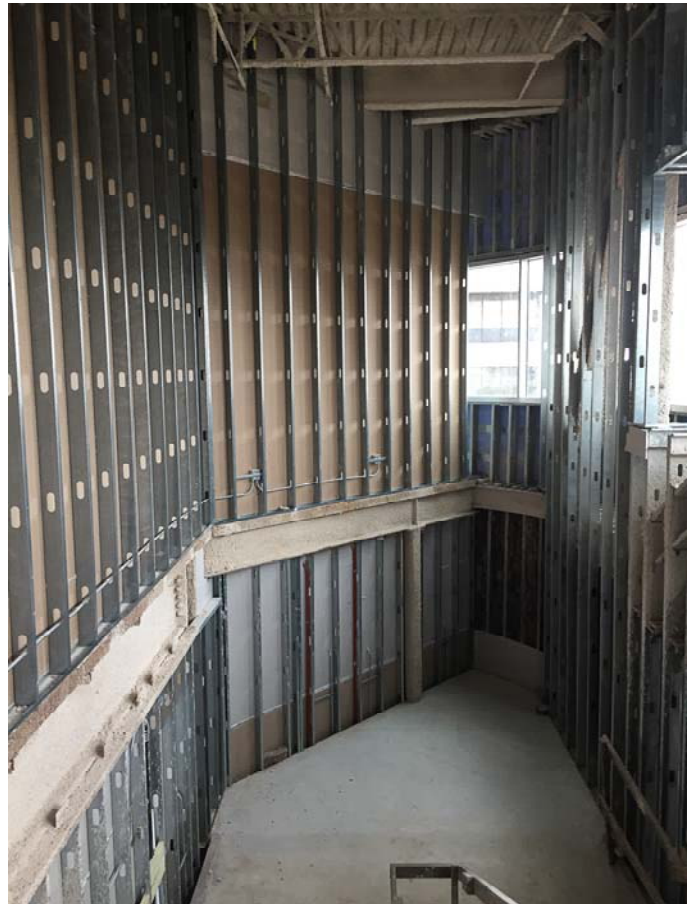

IMG_9871



IMG_9931



IMG_9935



IMG_9938



IMG_9942
