

---

# WHLC Architecture - Schwartz/Silver Architects

---

A Joint Venture

## CONSTRUCTION REPORT

---

Project: River Center Branch Library

Project No.: 11-025

Report No.: 031

Site Visit Date/Time: 03-08-2018

Location: Project Site; site visit and walk

Attendees: R. Roussel, T. Colomb, T. Mathis, M. Caillouet

Weather/Temp: High temp of 71 degrees, mostly cloudy, dry site

### Work in Progress/Observations:

- Tape and float is ongoing.
- Restroom tile work on the 4th floor is almost complete.
- The tile setting looks good and the grouting has not been completed.
- ACM panel along the south elevation is nearing completion.
- The vestibule steel work is getting cleaned up in anticipation for the intumescent coating to be applied.
- The ceiling fur down work continues with gyp. bd. and metal studs.
- The roofing work continues.
- The millwork mockup was approved on site with minor comments related to the laminate seam at the overhead cabinet once the doors are open.
- The intumescent coating was on site and being stored in the 1st floor of the library.
- The tile work in the toilet rooms was continuing on in the single toilet rooms and lower floors. The Sub Contractor was using the clips to bring the tile flush to the face of each adjacent tile. This installation was looking quite good.
- The HVAC is not running within the building
- All the material for the vestibule is on site in the front of the site.
- The ACM panel is still in progress.

(see attached photos)

Items/Questions:

Prepared by: WHLC Architecture, LLC.




IMG\_0273




IMG\_0274




IMG\_0275

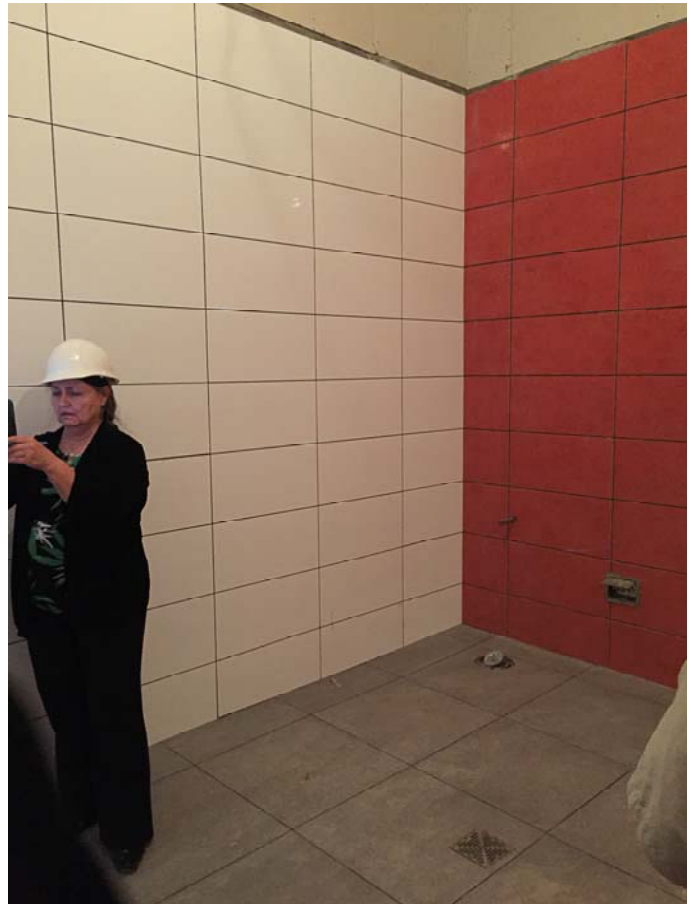

IMG\_0276

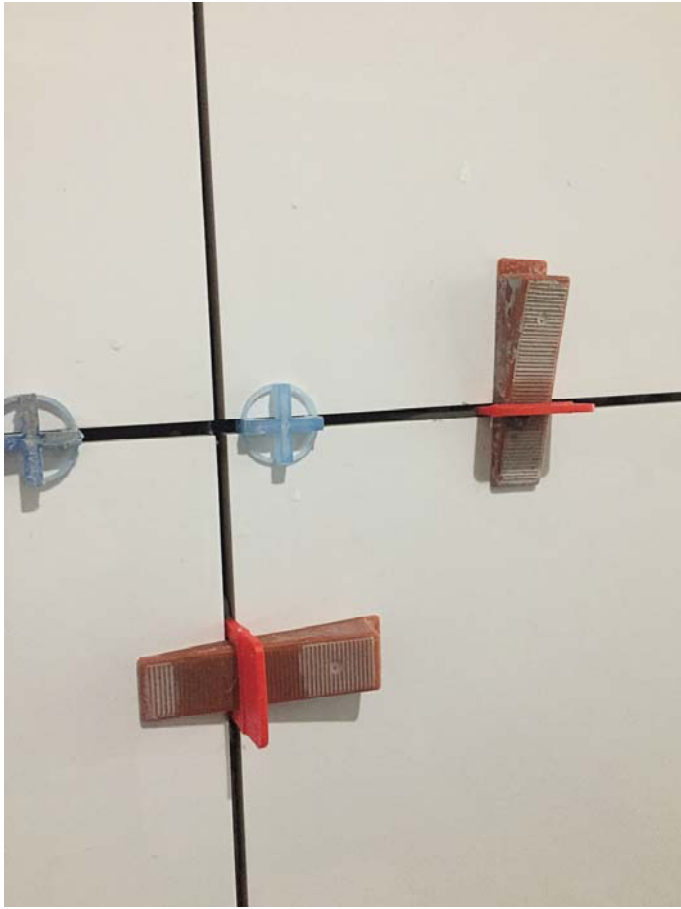

IMG\_0349

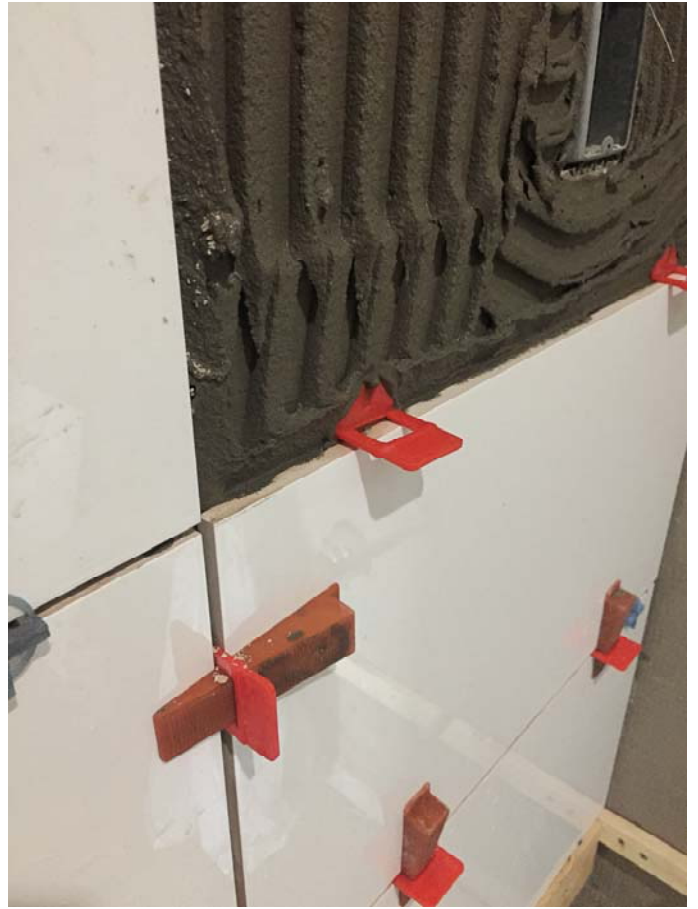

IMG\_0350



IMG\_0352



IMG\_0353
